

# MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 7-8-2020



**TOTAL AP REFRESH PROGRESS - 47% Complete**

**Watch**



OVERALL SCORE

**3.0/5.0**

MONTHS UNTIL WRAP-UP

TBD

Projected Project WRAP-UP DATE:

**TBD**


## POTENTIAL ISSUES/CONCERNS:

- Difficulty with finance to get more AP's as lead time planning is hampered by COVID-19
  - o Need to provide Dennis with AP rollout plan for budgetary discussions
- Timeline concerns with AP installs and building access
  - o Need to give proper lead time accounting for building access


## OVERVIEW

The month of June was dedicated to finishing building design work and planning for the start of concentrated AP deployment by identifying the most important buildings that need to be accomplished before the fall semester starts. At Jeanne's direction the Field Services team is working to identifying the common spaces and labs that will likely be the most occupied when school resumes. Westphal and Electric Shop are working to complete the wiring of the remaining designs submitted. The major focus going forward for Field Services will be on planning and deployment of AP's in the critical areas identified.

## AP Install Information

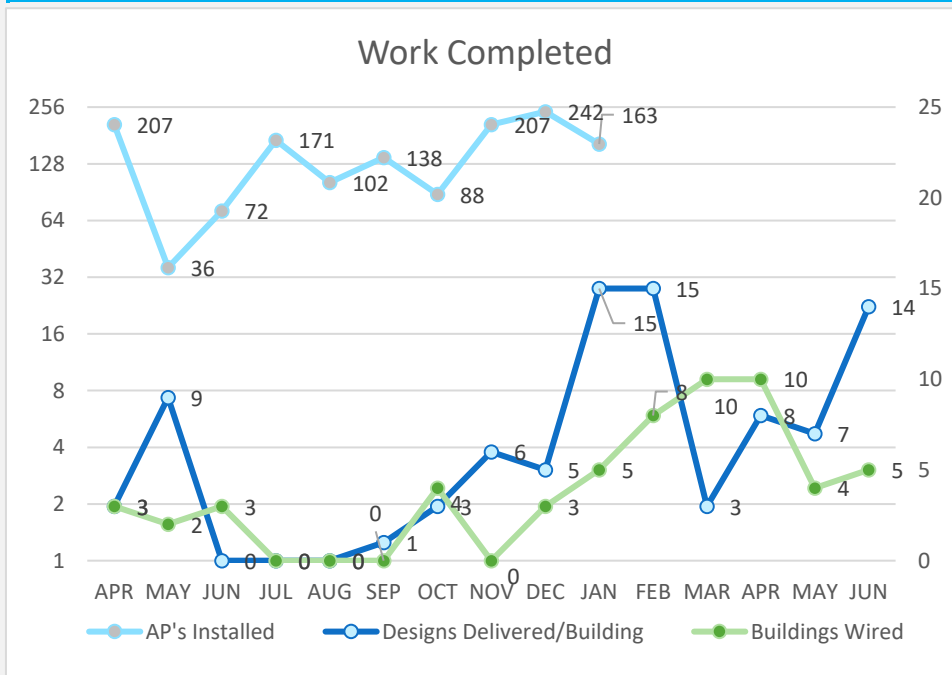

## Overall AP Installation Progress



**TOTAL AMOUNT OF AP'S INSTALLED  
3163 OUT OF 6792 = 47% INSTALLED**

## KEY PROGRESS

### New Designs Delivered (14)

- Russell Labs
- SMI
- MFCOB
- Biochemical Sciences
- Biochemical Labs
- Biochemistry Building
- MSC
- Babcock Hall
- Goodnight Lab
- Pharmacy
- 1220 Capital Court
- Wisconsin Primate
- Harlow Primate Lab
- Mechanical Engineering

### Electric Shop/Westphal Completed: (5)

- Russell Labs
- Computer Aided Engineering
- Bascom Hall
- Biotron
- AOSS

### Electric Shop/Westphal in Progress (14)

#### Notes:

- **Completed 0 buildings for a total of 0 AP's installed in June.**
  - o Meat and Muscle AP deployments – though not part of this project
  - o Field Services is working to identify locations for AP deployments and doing prep work for those locations
  - o 4 buildings left to submit for designs – all 1 for 1 replacements
  - o July will be a focus of AP deployments

# MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 7-8-2020

