

MONTHLY PROGRESS REPORT – UW Campus Wireless Upgrade Project - 1-7-2021



TOTAL AP REFRESH PROGRESS - 53% Complete

Watch



OVERALL SCORE
3.5/5.0

MONTHS UNTIL WRAP-UP
TBD

Projected Project WRAP-UP DATE:
June 30, 2021

POTENTIAL ISSUES/CONCERNS:


- Heightened sensitivity to install presence with students/faculty returning to campus
- Ongoing community spread of COVID and potential outages relating to illness.

OVERVIEW

Another month of great progress for AP deployments. Despite the short month with holiday outages, December was a continuation of the strong November with the Field Service team working on AP unboxings and configurations and Westphal doing new AP deployments. The teams were able to deploy 968 new AP's in 14 buildings. New AP's and mounting kits were also ordered, delivered and added to the work process queue. Part of the discussion before the break, to keep Westphal engaged, was to shift to smaller buildings for new AP deployment as we continue to process the new AP's. Electric shop is continuing on the building wiring, finishing a couple of larger buildings in December.

AP Install Information

Work Completed

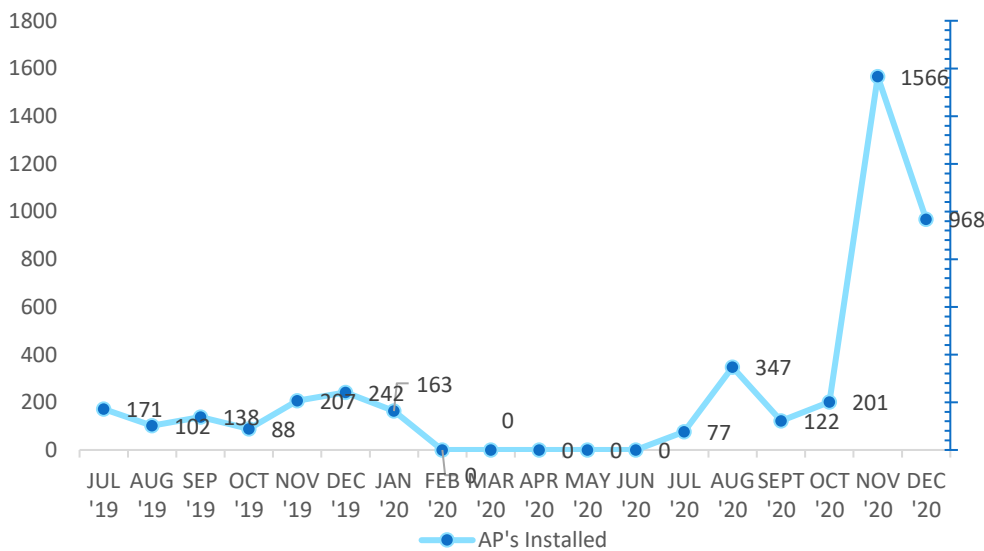

KEY PROGRESS


AP's Deployed (968)

Birge Hall	Chamberlain Hall
ECB	Computer Aided Engineering
Limnology	Material Science
Biotron Lab	WISC PIC
Psychology	School of Social Work
Waisman	Lathrop Hall
Law Bld	702 W. Johnson

Westphal AP building deployments prioritization list (8)

- Pharmacy
- AHBS
- Babcock Hall
- Ingraham Hall
- 21 N. Park
- Gen Bio
- Service Building
- Service Building Annex

Overall AP Installation Progress

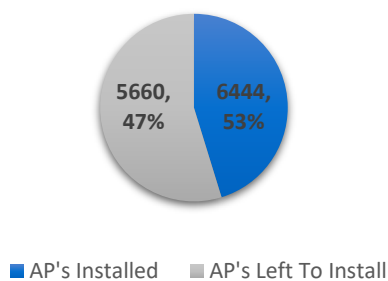

Notes:

- **Deployed new AP's in 14 buildings for a total of 968 AP's installed in December.**
 - o New AP's and mounting kits delivered
 - o Focus on some of the smaller buildings for AP's
 - o Electric shop continuing to wire larger buildings.

**TOTAL AMOUNT OF AP'S INSTALLED
6444 OUT OF 12104 = 53% INSTALLED**
